



FLORIDA DEPARTMENT OF TRANSPORTATION - DISTRICT FOUR


A1A Improvements Project in Hollywood

A1A from Sheridan Street to Monroe Street

Financial Project ID Numbers: 432323-1-52-01

MONTHLY PROJECT UPDATE AND UPCOMING ACTIVITIES

The Graph below depicts the project’s status of completion in green, while the blue depicts anticipated progress of completion in the month of April. Activities the contractor will be working on this month include the installation of sidewalk pavers on the east side of the road, curb and gutter, conduit, asphalt sidewalk on the west side of the road, and drainage.

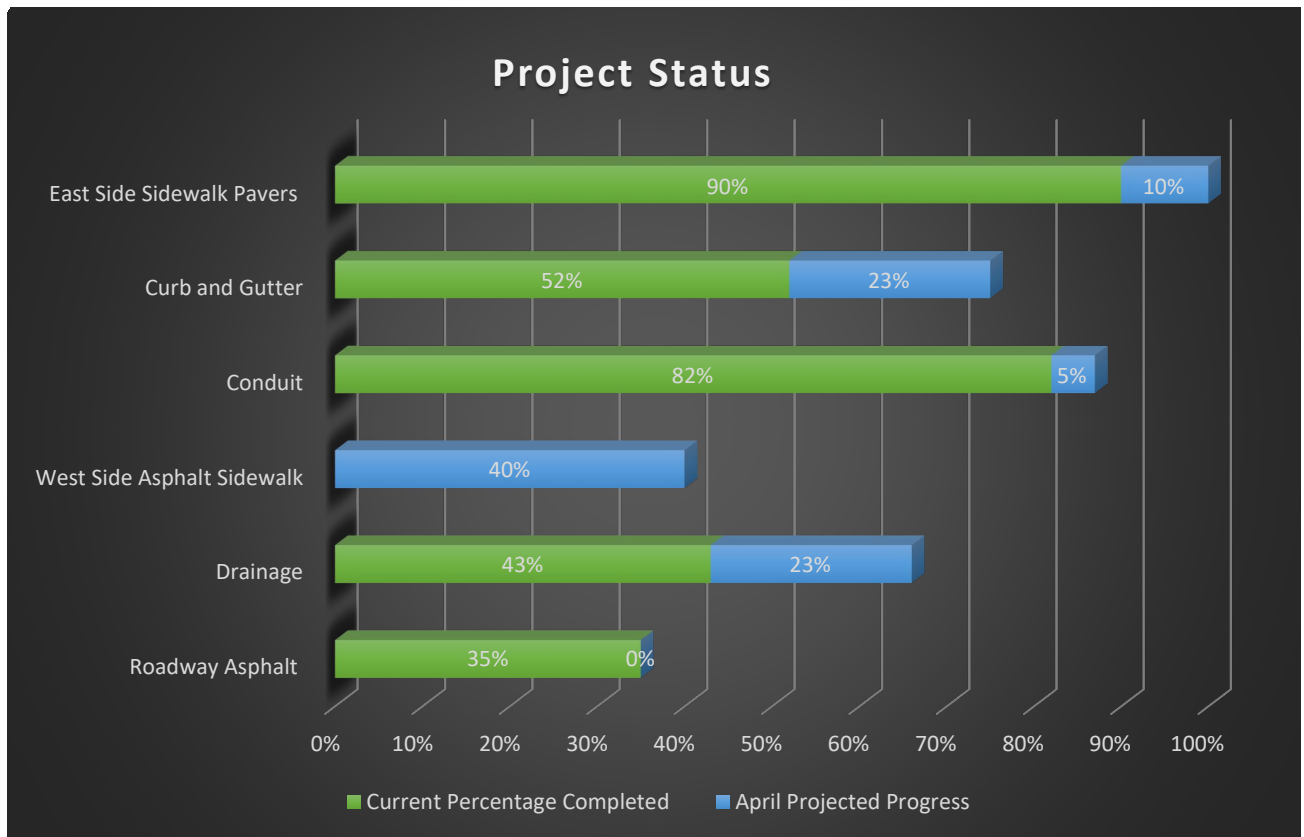

CONTACT INFORMATION

Heidy Cuevas, P.E. Construction Project Manager

Phone: (954) 958-7653

Email: Heidy.Cuevas@dot.state.fl.us

Rebecca Guerrero–Community Outreach Specialist

Phone: 954-940-7605

Email: rguerrero@corradino.com

Construction Cost: \$9,366,292.09 Construction Start Date: October 9, 2017 Anticipated Completion: Summer 2019
