



## FLORIDA DEPARTMENT OF TRANSPORTATION - DISTRICT FOUR

### 95 Express Phase 3B-1

I-95 from south of SW 10th Street to south of Glades Road

Financial Project ID Numbers: 433108-6-52-01 & 433109-4-52-01

## Construction Schedule for I-95 Widening at Hillsboro Canal Bridge

Construction activities for the widening of I-95 and the complete replacement of the Hillsboro Canal Bridge at I-95 in Boca Raton are underway. This full bridge replacement is being performed in three phases:

**Phase 1/northbound:** demolish existing northbound bridge, perform dredging activities, reconstruct bridge and widen I-95 northbound


⇒ Phase 1 northbound bridge construction was COMPLETED October 2019.

**Phase 2/median:** demolish existing median bridge, perform dredging activities, reconstruct bridge in the median of I-95

⇒ Phase 2 median bridge construction was COMPLETED May 2020.

**Phase 3/southbound:** demolish existing southbound bridge, perform dredging activities, reconstruct bridge and widen I-95 southbound

⇒ Phase 3 southbound bridge construction BEGAN May 7, 2020 and is 75% completed as of mid-August, with anticipated completion of December 2020. Pile driving activities and beam setting activities for the entire project were completed on July 17 and August 11, 2020, respectively.

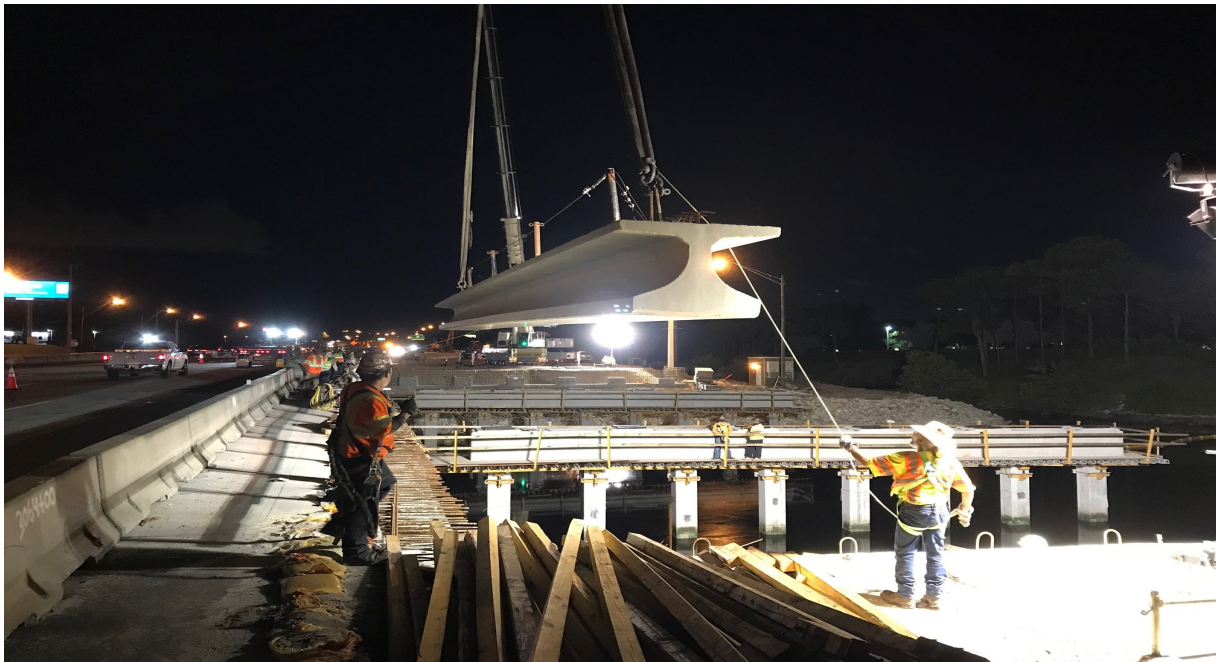

*Final beam setting operations along I-95 southbound for complete reconstruction of the Hillsboro Canal bridge*

This bridge replacement will also increase vertical clearance for vessels to 12 feet from mean high water elevation from the current clearance of 8 feet. Permitted hours of work at the Hillsboro Canal are 7 a.m. to 6 p.m. Monday through Friday and 8 a.m. to 7 p.m. on Saturdays. No work is permitted on Sundays or holidays. Boat access will be maintained at all times, with intermittent closures necessary to ensure safety during specific construction activities. All in-water construction activities will be coordinated with the United States Coast Guard and a notice to mariners will be sent out prior to any significant closures or impacts at this location.

### CONTACT INFORMATION

**William Grey, P.E. - FDOT Project Manager**

William.Grey@dot.state.fl.us or 954-940-7511

**Andrea Pacini - Community Outreach Specialist**

apacini@corradino.com or 954-299-6561

Construction Cost: \$102 million

Construction Began: January 19, 2018

Anticipated Completion: Spring 2022
