

**State Road (S.R.) A1A  
FDOT Construction Update**

---

**From South of S.R. 802/Lake Avenue  
to North of Ibis Way**

**From North of Emerald Beach Way  
to South of S.R. 704/Royal Palm Way**

---

**Town of Palm Beach  
Council Meeting  
October 14, 2025**



# 447663-1-52-01 (E4X31)

## S.R. A1A from South of S.R. 802/ Lake Ave. to North of Ibis Way



*Project Start – May 3, 2025*



*Construction Cost – \$5.96M*



*Anticipated End Date – Summer 2026*



*Contractor – The Stout Group, LLC*



# New Concrete Pathway – West Side of Roadway

S.R. A1A from South of S.R. 802/Lake Ave. to North of Ibis Way

Northbound




Southbound



# Palm Beach Par 3 – Mast Arm Base and Pathway Progress

S.R. A1A from South of S.R. 802/Lake Ave. to North of Ibis Way

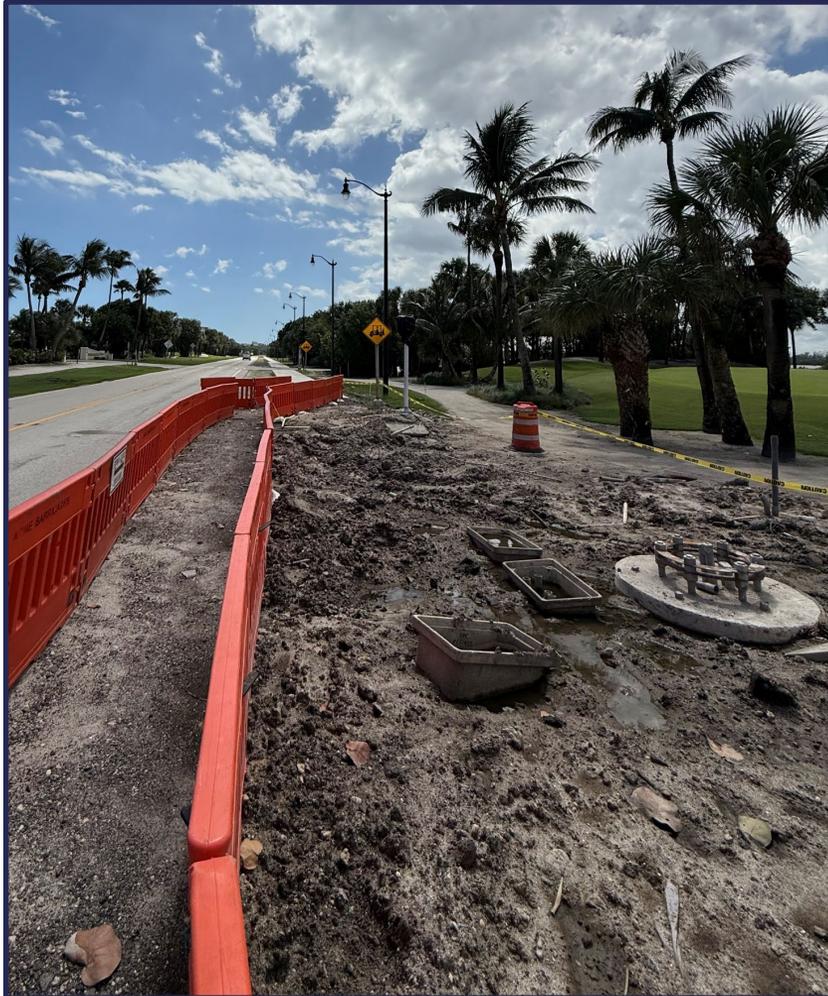

# Work anticipated now through Spring 2026

S.R. A1A from South of S.R. 802/Lake Ave. to North of Ibis Way



Continue concrete pathway installation on west side of roadway



Begin roadway shoulder widening (2 to 3 feet in each direction)



Continue pedestrian signalization at the Palm Beach Par 3



Maintain pedestrian access during construction operations

# 446175-1-52-01 (E4W84)

## SR A1A from North of Emerald Beach Way to South of SR 704/Royal Palm Way



*Project Start – May 27, 2025*



*Construction Cost – \$8.25M*



*Anticipated End Date – Late 2026*



*Contractor – Halley Engineering Contractors, Inc.*



# New Pavement – N of Emerald Beach Way to S. County Rd.

S.R. A1A from North of Emerald Beach Way to S.R. 704/Royal Palm Way



# Paving/Sidewalk Ongoing – S. County Rd., S of Hammon Ave.

S.R. A1A from North of Emerald Beach Way to S.R. 704/Royal Palm Way



# Work anticipated now through Thanksgiving 2025

S.R. A1A from North of Emerald Beach Way to S.R. 704/Royal Palm Way



Complete final paving & striping on S.R. A1A from the S.R. 80/Southern Blvd. traffic circle to S. County Rd.



Complete sidewalk removal & replacement on S. County Rd. from south of Hammon Ave. to S. Ocean Blvd.



Prep work zone to minimize impacts through season



Clear work zone of debris and maintain conditions through season

# Work anticipated from Thanksgiving 2025 to Spring 2026

S.R. A1A from North of Emerald Beach Way to S.R. 704/Royal Palm Way



Complete utility subsurface exploration




Modify light pole and mast arm foundations as needed



Finalize material procurement including new traffic signal mast arms



Prepare for Midtown construction operations beginning in Spring 2026



# THANK YOU

---

Questions & Comments
